


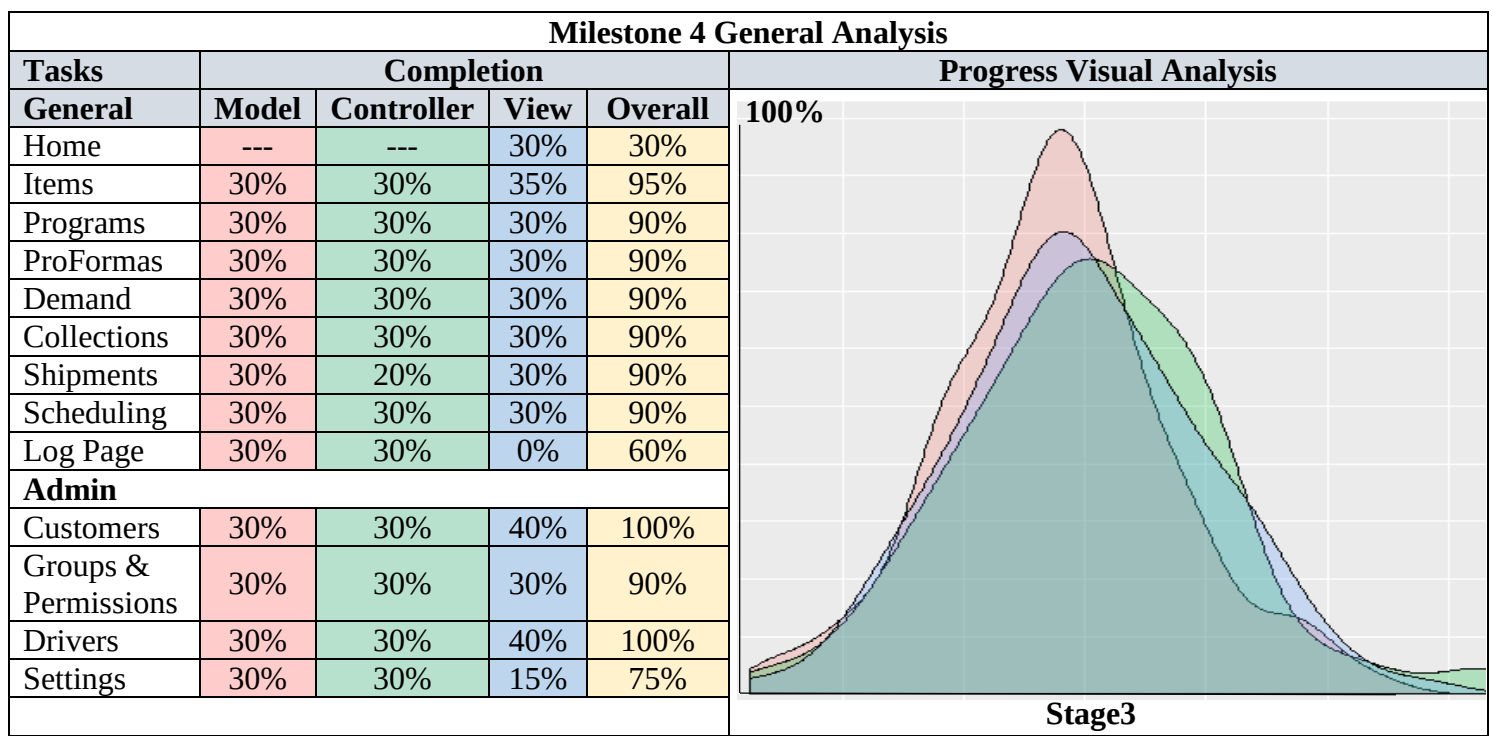

The “Controller” completion percentage during the system implementation has increased dramatically throughout the completion of the milestone IV/ stage-3. Previously, there were two issues that were affecting the completion progress of some controllers for the stage-3 of this project. These issues were related to the data and interface, which were addressed in the following manner:

- Data: there are only two datasets missing, the Royalty tables and the Excess Inventory. All data fields missing from the Item import dataset are currently being fixed by both parties, TI and LTB.
- Interface: The rate at which the interface implementation progress has been increasing is promising. Therefore, the lag that we experienced during the interface implementation should not affect the completion of the system evaluation stage as scheduled if the contribution rate continues the same or higher.

In the progress visual analysis, the deadline and tasks completion are the factors used to measure the current performance. Even though the View progress percentage is increasing dramatically, we are still lagging by less than 20%. Issues affecting the View’s completion are currently being addressed by both parties LTB and TI, and its completion is increasing at a satisfactory rate.


Solutions:

- Obtain the data missing within a week
- Address all issues pertaining to the View’s implementation completion during the System Evaluation stage
- Continue the distribution of the interface development tasks within the first two weeks of the next stage

Goal:

The goal is to address the current gap as fast as possible and finish the System Evaluation stage as specified in the project outline. In order to achieve this, we must finish all interface development missing tasks while evaluating/improving those already implemented. Also, the contribution rate at which all tasks are being completed must remain increasing at the rate which it currently is.

4 System Implementation		
1	Implement User Based System Model	
1	Groups Permissions Assignments	Complete
2	Users Permissions Assignments	Complete
2	Implement Strategy Plan System Model	
1	Programs	Complete
2	Proformas	Complete
3	Demand Solution	Complete
4	Collections	Complete
5	Items	Complete
6	Shipments	Complete
7	Scheduling	Complete
8	Logs	Incomplete
9	Settings	In-Progress




In-Progress Tasks:

A model and constructor has been built for all tasks in-progress, however, the GUI for Settings is still under development because some features are still being designed.

Complete Tasks:

A model and constructor has been built for these objects. The implementation of the constructor was possible because most data sources have been provided and the interface implementation has increased dramatically.

Graphical User Interface		
1	Home page	In-Progress
2	Items page	Complete
3	Programs page	In-Progress
4	Proformas page	In-Progress
5	Demand page	Complete
6	Collections page	Complete
7	Shipments	Complete
8	Scheduling	Complete
9	Logs	Incomplete
10	Settings	In-Progress
11	Admin settings	In-Progress

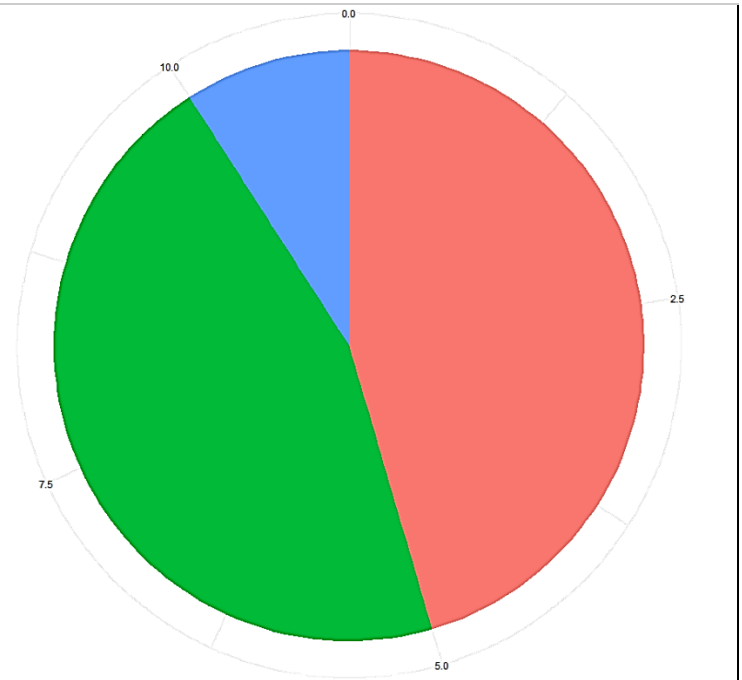


Incomplete Tasks:

These tasks are low priority and can easily be addressed during the evaluation stage of this project.


In-Progress Tasks:

The tasks that are in progress are being currently updated. We expect to have all, or most of, the tasks completed within the first two weeks of the next stage. In this stage, improvement and multiple evaluation will be performed for quality assurance to meet the client's needs and expectations.

GUI DEVELOPMENT BREAKDOWN

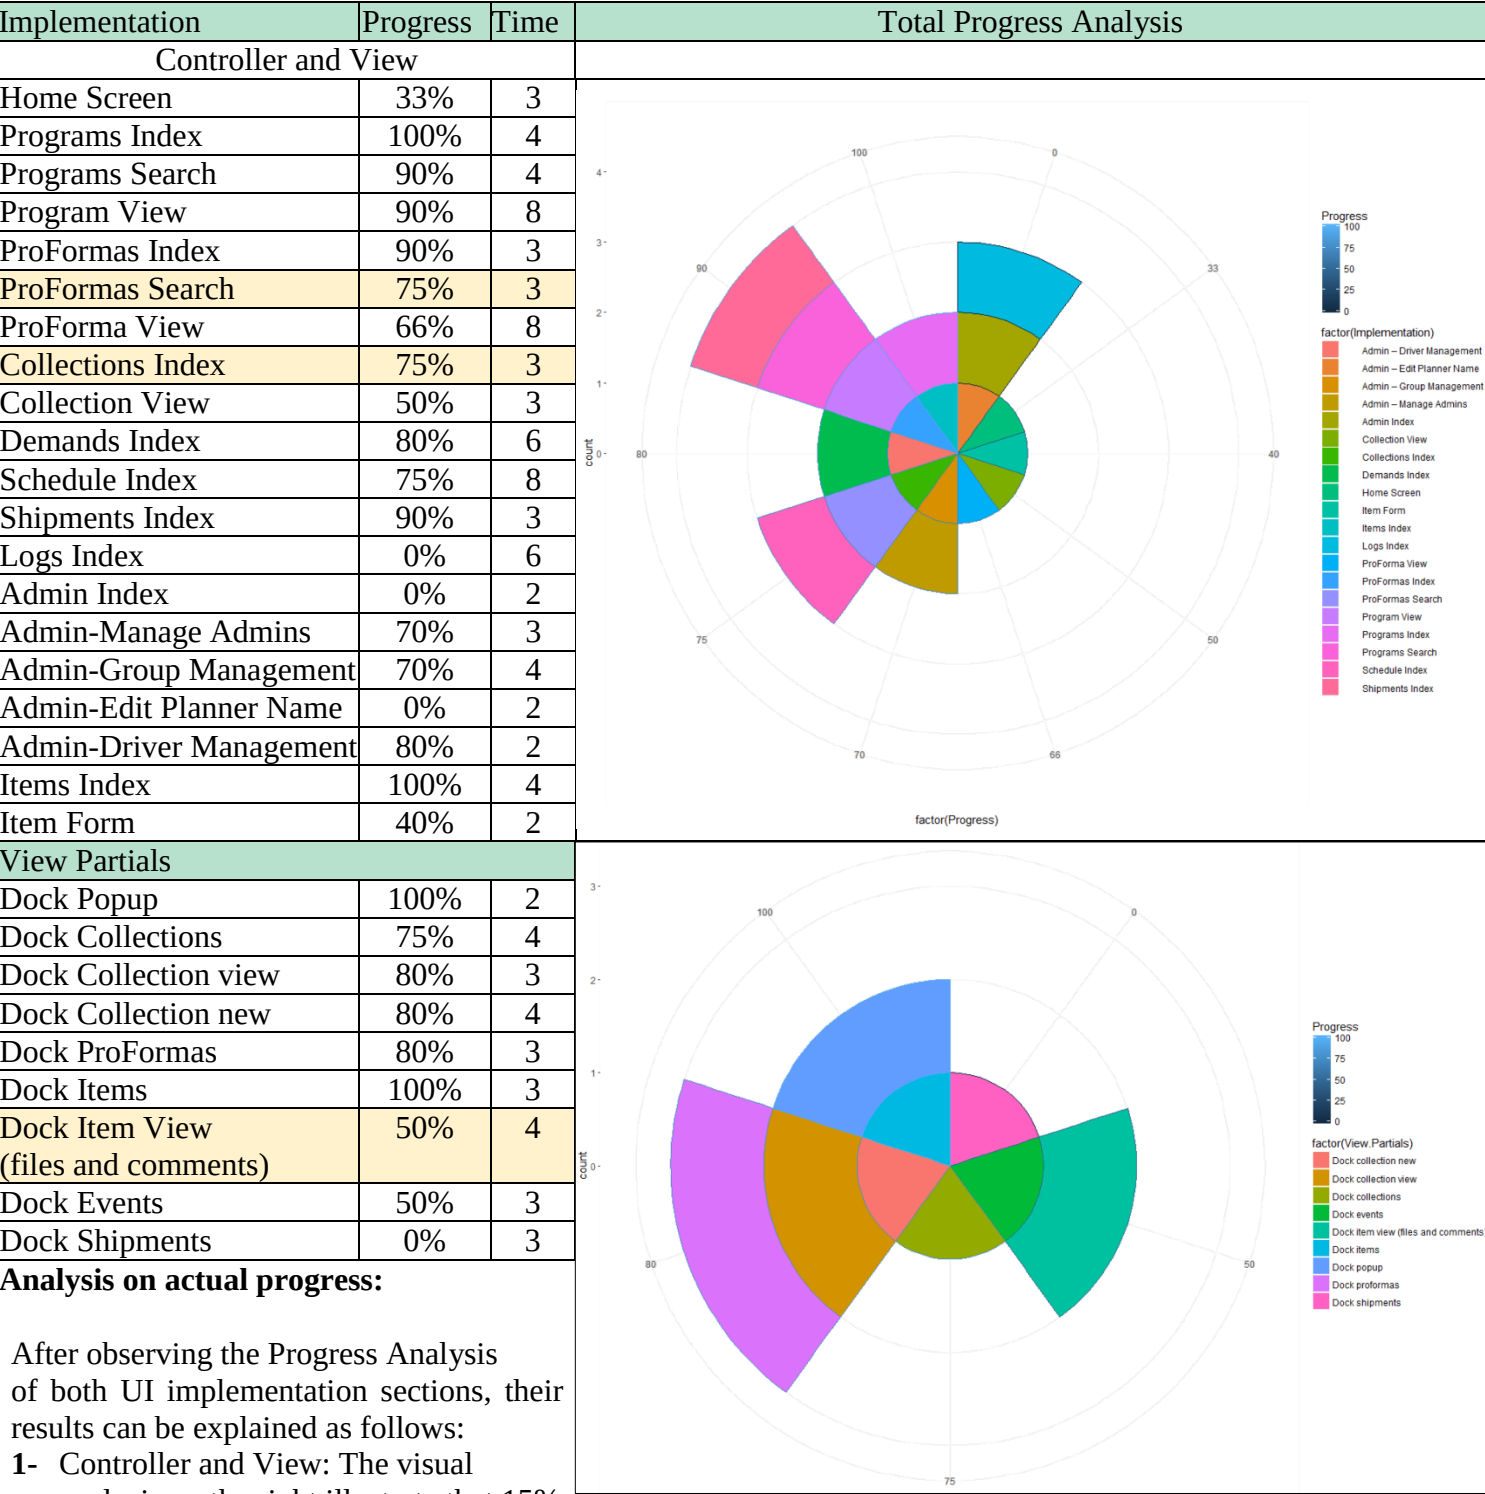

CONTRIBUTION PLAN

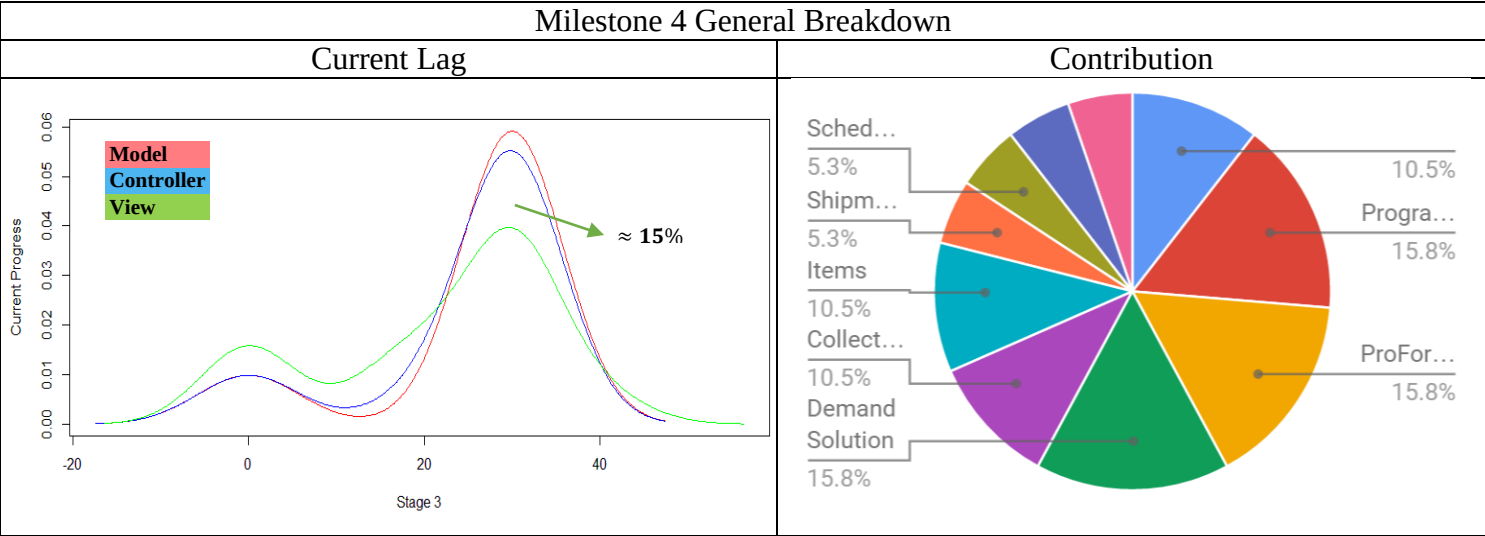

Plan Description:

In order to make up for the lag experienced in the stage-3 of this project, it will be necessary to combine tasks and perform the tasks in stage-4 in a specific order. Tasks that have already been done need to be evaluated first to allow other tasks, that are currently in progress, be finished. Tasks that have not been finished, by the time all done tasks had been evaluated, will need to be finished and evaluated at the same time.

Focus:

It is important to keep the same priority as in Stage-3 such as Proforma, Agreements, Demand Solution and Items. It is even more important to make sure that the logic among these objects is consistent and understood by the LTB party, it would be very helpful to get their feedback during the evaluation process of the system.

Goal:

To provide the client with an application capable of performing tasks that are currently delaying their sales process. Once again, the completion of Agreements, Proformas, Demand Solution and Items is highly important for this project; these objects contain the tasks that are needed the most during their sales process. An added percentage distribution, as previously stated - top-right image, should achieve the proposed plan to close the lag specified in the GUI Development Breakdown. On the other hand, as illustrated in the top-left image, more emphasis will have to be put towards the completion of the Interface, especially for the objects with a high priority, to reduce the 15% gap.
