


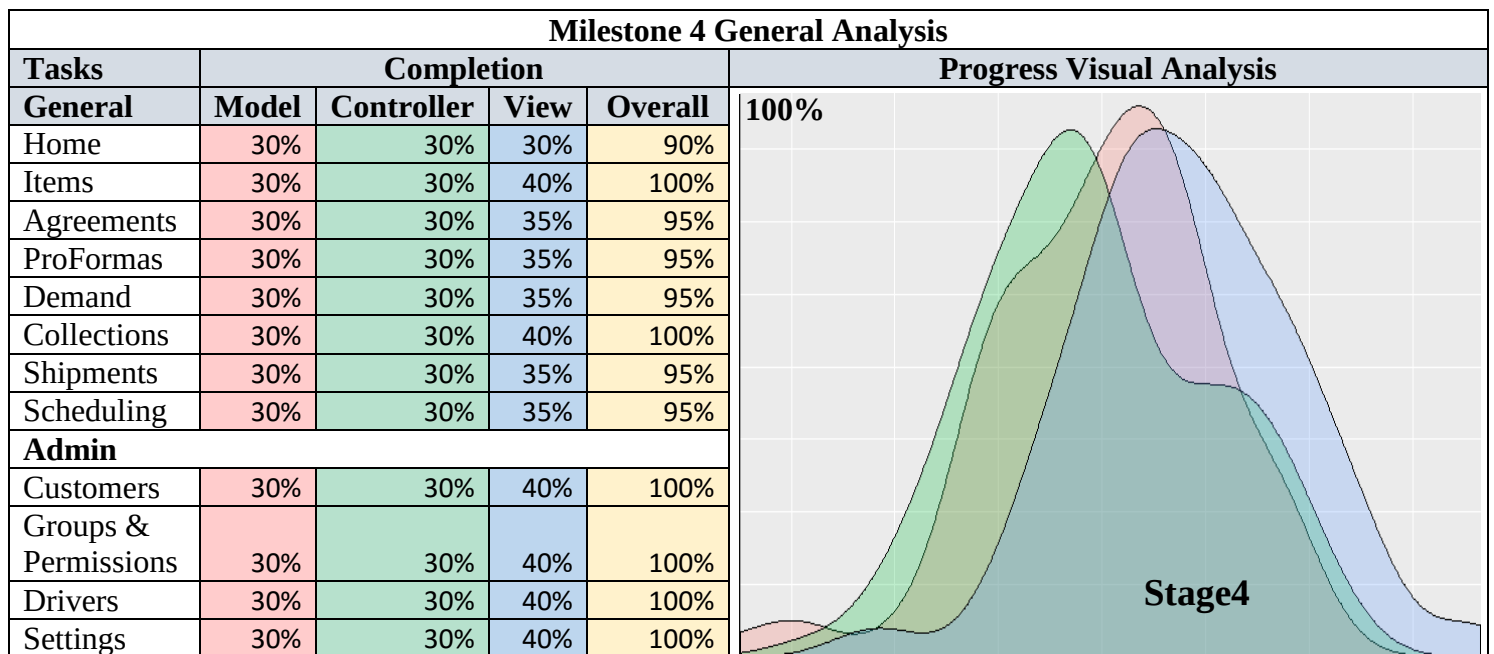

The Model, Controller and View for this project have been completed. Each feature in this application, referencing to the tasks in the table above, has been individually tested. The system is able to perform the following tasks:

• Items & Demand Solution ○ Search, Filter & View • Agreements & ProFormas ○ Search, Filter & View ○ Create, Edit & Save • Collections, Shipments & Scheduling ○ Search, Filter & View ○ Create, Edit & Save • Customers, Drivers ○ Search, Filter & View ○ Create, Edit & Save	<i>Search, Filter & View Objects:</i> Users are able to search, filter and view objects such as Item, Agreement, ProForma, Collection, Shipment, Customer and Driver. These functionalities have also been integrated among objects so users can search, filter and view other objects, such as items, while creating a ProForma, Agreement, among others.
	<i>Create, Edit & Save Objects:</i> Users are able to create, edit and save objects such as Agreements, ProFormas, Collections, Shipments, Schedulings and Drivers. These functionalities are not integrated among objects because at this stage it is not a requirement. Therefore, users must access the object directly in order to create, edit and save it.
• Groups-&Permissions & Settings ○ Create, Edit, Add • Collections, Drivers & Item ○ Add	<i>Add Objects:</i> Lastly, users are able to add objects, such as items, collections and drivers. These are integrated functionalities that are used to add objects, such as items, from a dock to a Program, ProForma, Collection and so on.


In the progress visual analysis, the deadline and tasks completion are the factors used to measure the current performance. We were able to close the gap from Milestone IV and completed all features implementation during the evaluation process in Milestone V. However, we are still lagging because of the tradeoff from both milestones. Even though we were able to individually test all features, we still need to finish testing these features collectively since these must be interactive. This is a process that will take longer than testing individual features because it will include user’s feedback, such as the ProFormas and Agreements approval process.

Solutions:


This is the final stage of the project, therefore, the only solution left to eliminate the current lag and meet client’s needs is to extend the system evaluation stage in order to test all features properly. In order to achieve this, we need to implement the Agreement & ProForma Approval process and fix all bugs, especially those pointed out by LT BSP.

Goal:

The goal is to make the current application “smart” by allow users to create, save, approve and reject Agreements and ProForma through the approval process. Similarly, users should be able to use this application to monitor customers and sales performance, among other tasks.

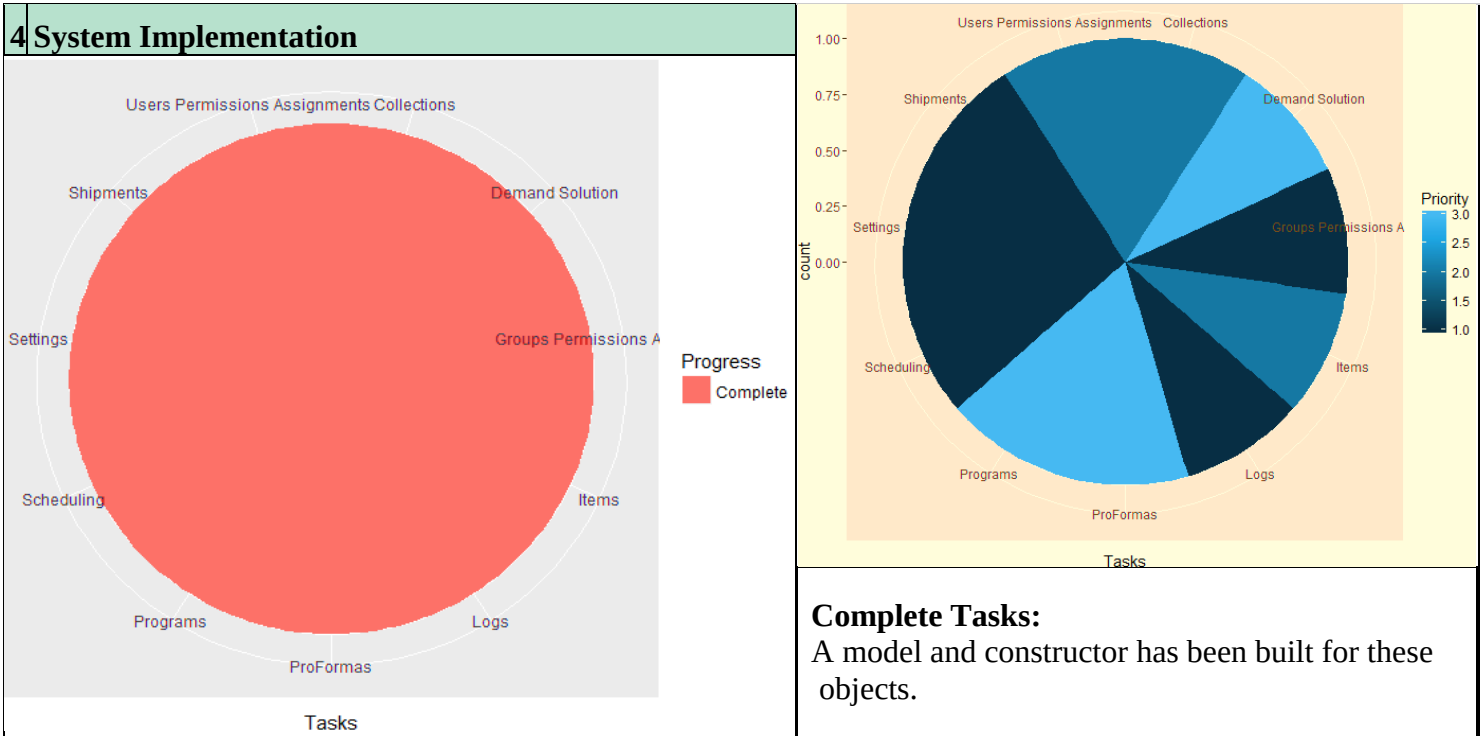


The implementation of some objects, such as demand solution, Scheduling and others, had to be completed during the system evaluation process because of the lag that we were experiencing – this lag was explained in previous progress report. The image to the right shows the priority levels given to the objects for completion, and the image to the left shows the completion level of this. As we can see in the left image, we have successfully implemented and tested all objects. Currently, we are working on the Agreement and ProForma Approval process. This is a separate process and, once done, it will be explained along with the application usage guide.

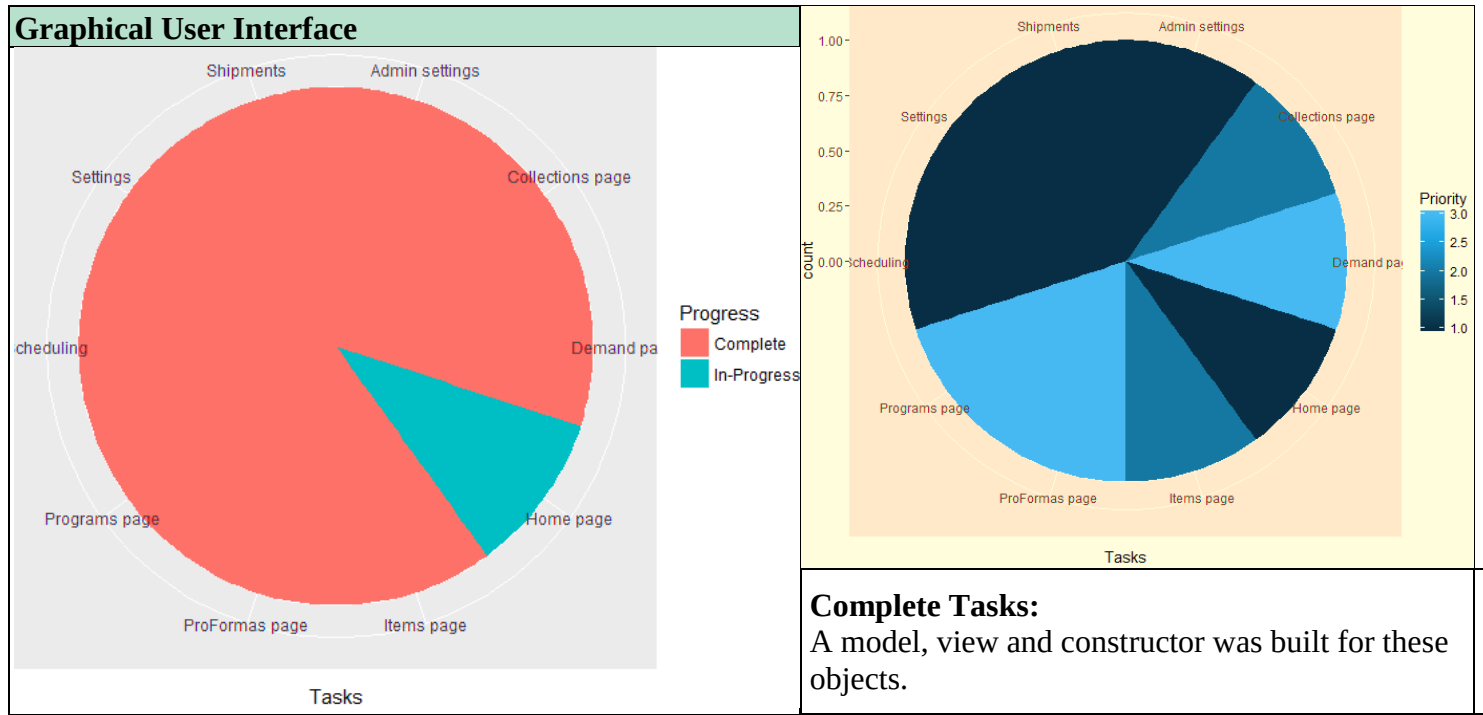

Similarly, the GUI or view of some objects have been completed during the evaluation process. The image to the right display the priority which each view was completed. The image to the left displays the view completion level. As we can observe, the only object view that is currently in progress is the Home Page. The reason to this is because we still have not agreed with the client what exactly will be in the Home Page. However, this will be a very easy accommodation for the client as we can easily access the controllers of whatever objects the client decides to have in the Homepage, and design it as per their request and needs.

GUI DEVELOPMENT BREAKDOWN

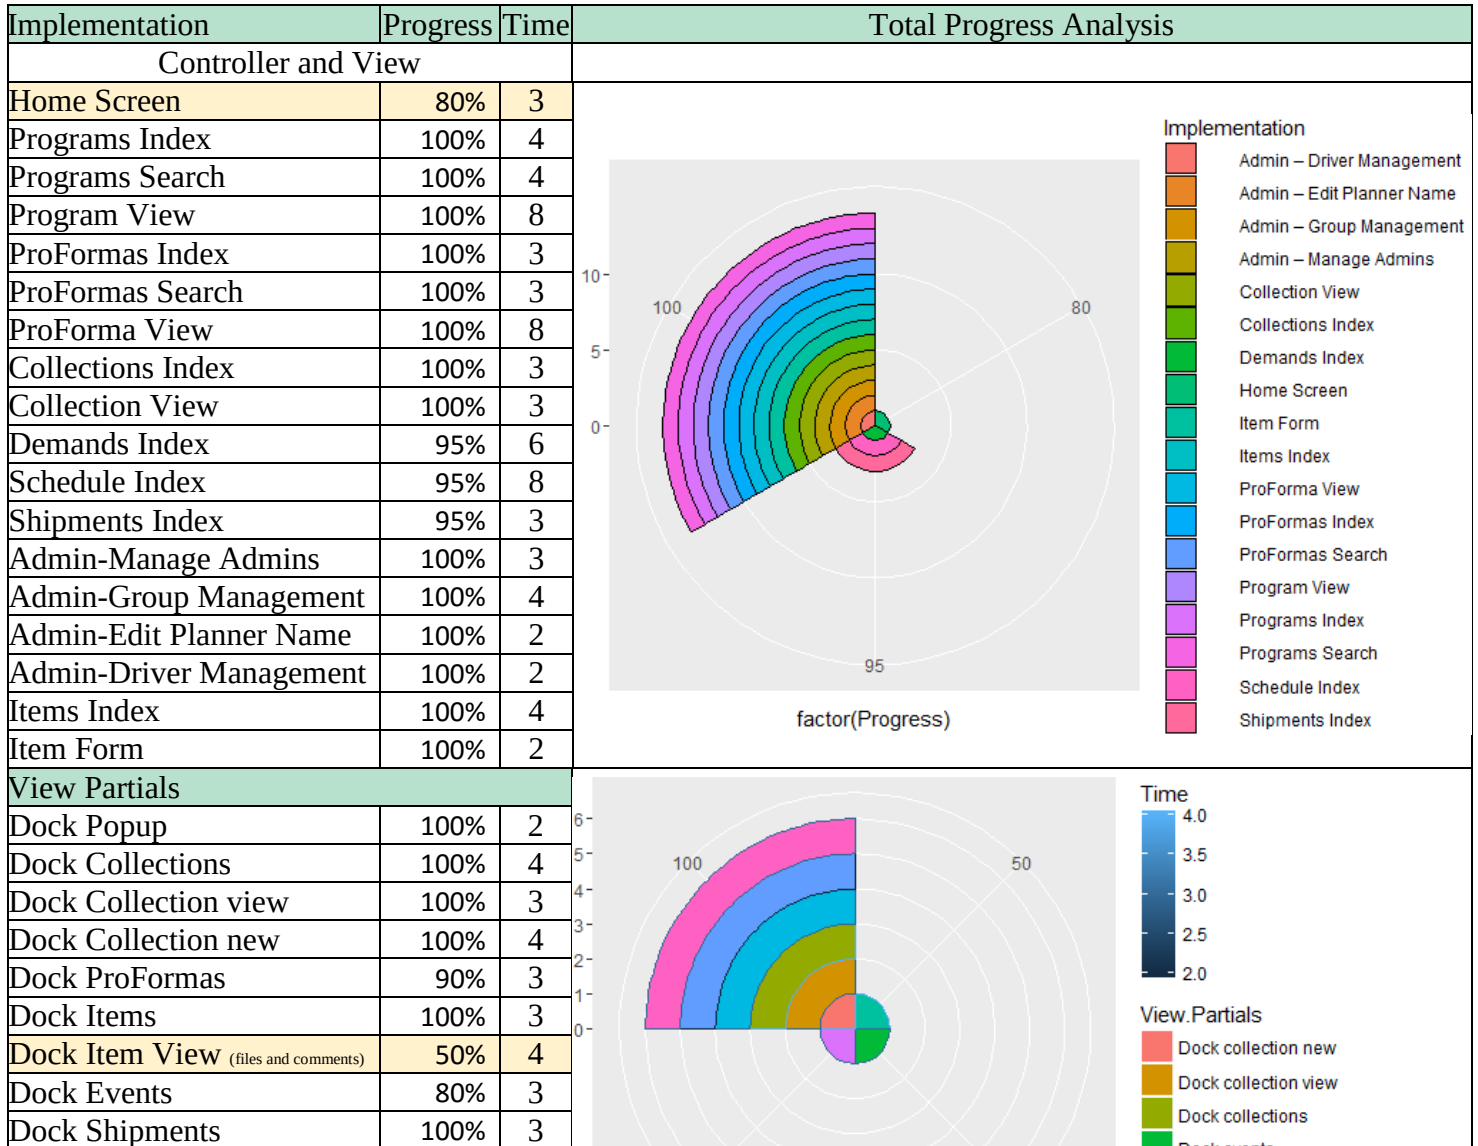

Analysis on actual progress:

After observing the Progress Analysis of both UI implementation sections, their results can be explained as follows:

1- Controller and View: The visual

analysis on the right illustrate that 3% of the tasks are not 100% but 95%. 2% of these tasks are fixes that have already been applied to other objects and need to be applied to these. The remaining 1% is directly related to the Dock Events. Overall, based on the observation in the top-right image progress analysis we can say that this section is complete and must focus in finishing testing and debugging.

Tasks:	Fixes in Progress
- Demand →	Dock
- Schedule →	Dock Event
- Shipments →	Remove Items


It is important to highlight that these tasks are very easy to fix and are not currently affecting the performance of the project. Therefore, there priority level is considered very low as there are other tasks (more important) that need to be addressed.

2- View Partial: The visual analysis on the right illustrate that 3% of the tasks are not 100%. 2% of these tasks are directly connected to the third task – the Dock Item View. Once this task is complete so will the 2% remaining tasks.

Tasks:	Fixes in Progress
- ProForma →	Item files and comments
- Dock Event →	Add Items & Collections
- Dock Item View →	Files and Comments

Similarly, to the tasks above, these tasks are not of high priority. Therefore, unless specified by the client in the bug sheet these tasks will be addressed last.

CONTRIBUTION PLAN

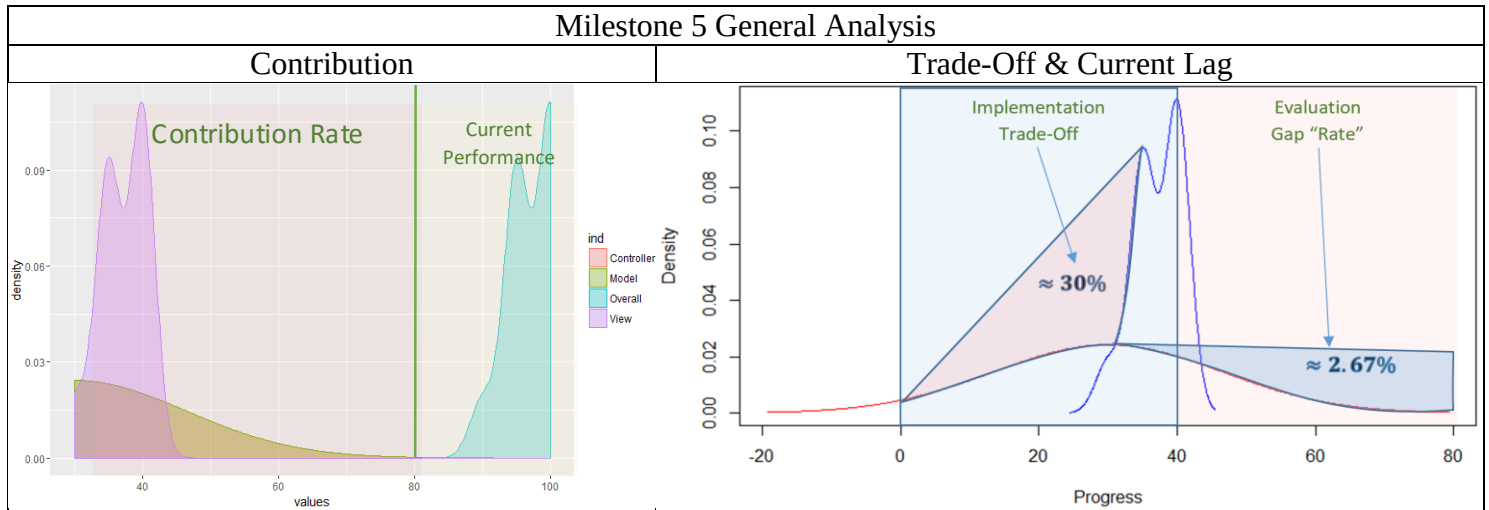

The contribution plan to reduce the gap from stage-3 and meet both stage-3 and stage-4 goals of this project had a trade-off effect. In other words, we were able to eliminate the gap and complete all tasks missing from the implementation process. However, the time and effort traded into the implementation process caused a gap during the evaluation process of the system. Unfortunately, this was the only way to proceed because in order to evaluate the system all features must be functional. The trade-off utilized about 30% of time and resources planned to be used during the evaluation of the system, inflicting in this way a 11% lag at a 2.67% rate. Currently, the rate is decreasing as all tasks have been completed and the primary focus is the evaluation and improvement of the system.



The image to the left displays the contribution margin during the stage 3 and stage 4 of this project. All objects, from the implementation process, that were completed during the stage 4 of this project belong to the view. As you can observe, the contribution to the completion of these tasks has the highest peak. On the other hand, the contribution of the system evaluation and improvement decreased as most time and resources were, and needed to be, utilized to make the In-Progress objects functional for evaluation and improvement purpose. The image to the left displays exactly how in the trade-off we utilized about 30% more of time and resources to complete In-Progress tasks. Also, it displays the highest lag rate we currently reached because of the trade-off and previous lag.

Plan Description:

The plan consists of three steps. First, address the needs of the client by fixing bugs discovered and reported by the client. Second, implement the Agreement & ProForma Approval process. Lastly, follow the tasks priority level (image to the right) to fix bugs reported by the team and improve the system.

Focus:

We should keep focusing on bug sheet, and making the current application “smart” to allow users to approve and reject Agreements and ProForma through the approval process.

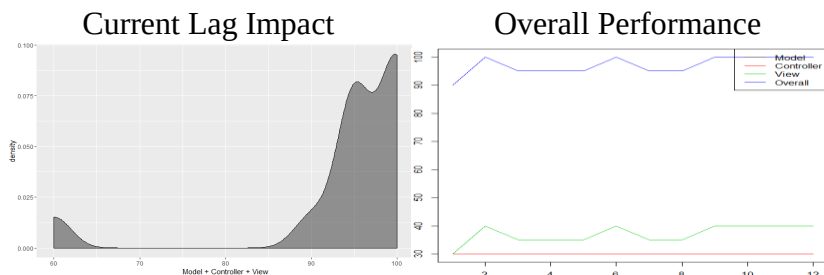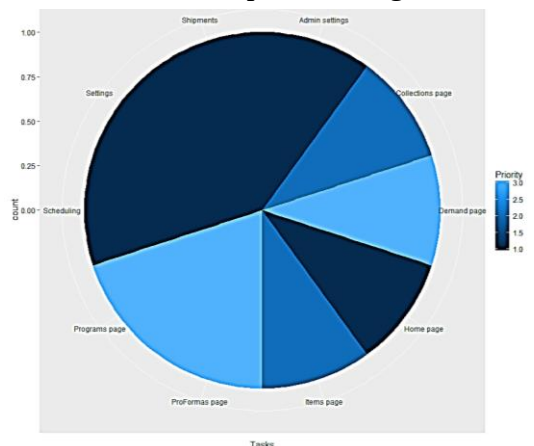

Goal:

As you can see in the left image, there was a huge lag caused by the trade-off and previous lag. However, after the completion of all tasks our current performance has hit its maximum – second left image. As mentioned above, in order to mediate with this lag and properly complete

the evaluation and improvement stage of this project and meet current goal, 2-3 weeks is required. The current goal is to provide the client with an application capable of performing tasks that are currently delaying their sales process. Once again, the completion of Agreements & ProFormas approval is highly important for this project due to its high demand during a sales process.
